

HiTech - Anand Niketan

Ahmedabad, India
PPC Report as per Feasibility Plan

Current week & Year

2023-12

20-03-202326-03-2023

Status

All

Critical Tasks?

All

Owner

All

Location

All


Date

15-10-2022

06-04-2024

Weekly PPC

Planned PPC Success1 Yes No PPC

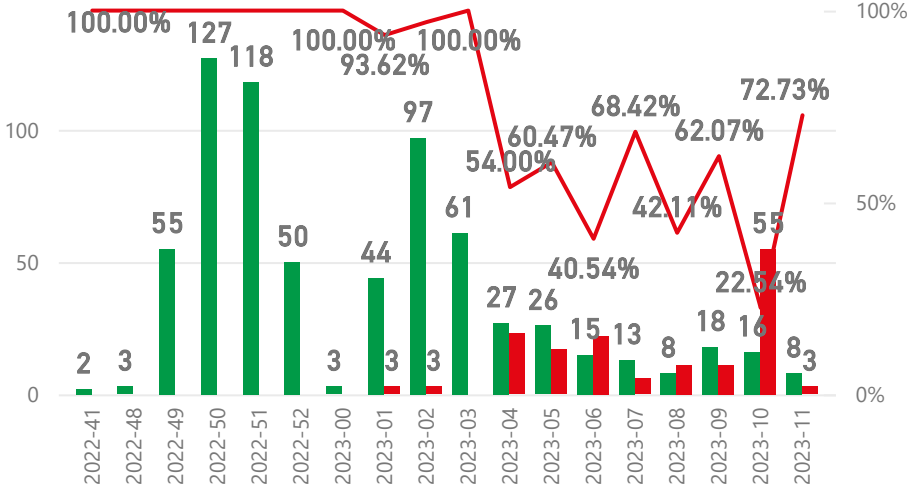

Weekly PPC

34.42%

2025

Total

657

Success

40

Early Finished

117


Late Finish

1328

Unsuccess

Daily PPC

Daily PPC Success Yes No PPC

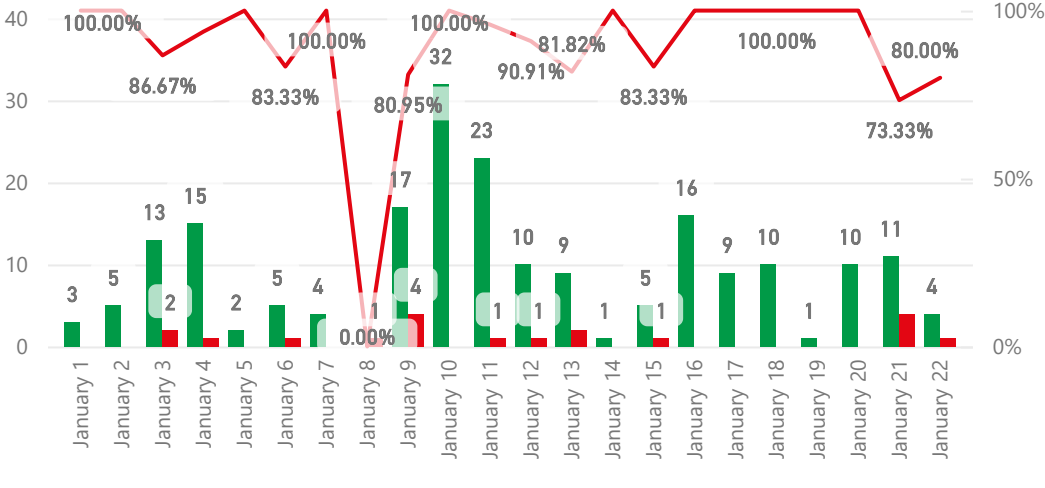

Daily PPC

33.38%

2025

Total

627

Success

49

Early Finished

138

Late Finish


1349

Unsuccess

Task Details

Task	Owner	Location	Part/Pour	Status	customField.Critical Task	Target	Actual End	percentComplete	Weekly PPC	Daily PPC Success	Daily PPC Success Sa
Site Survey & Mobilization	Rikesh Kumar Ravi	Hitech - Anand Niketan School Sarkhej		Complete	Yes	15-10-2022	15-10-2022	100	Yes	Yes	Sameday success
Approved Architectural & Structural drawings from Client and permission for excavation	Rikesh Kumar Ravi			Complete	Yes	16-10-2022	16-10-2022	100	Yes	Yes	Sameday success
(P3) Dressing & Levelling	Jayesh Lakhatariya	P3 Foundations/Raft Work	P3 Foundations/Raft Work	Complete	Yes	02-12-2022	02-12-2022	100	Yes	Yes	Sameday success
ATT & PCC	Praveen Kumar	P2 Footing CF1 (F-7)	Part 2	Complete	Yes	04-12-2022	04-12-2022	100	Yes	Yes	Sameday success
ATT & PCC	Praveen Kumar	P2 Footing R.Wall (D-O-1)	Part 2	Complete	Yes	04-12-2022	04-12-2022	100	Yes	Yes	Sameday success
ATT & PCC	Praveen Kumar	P2 Footing F-02 (M-9)	Part 2	Complete	Yes	05-12-2022	05-12-2022	100	Yes	Yes	Sameday success
ATT & PCC	Praveen Kumar	P2 Footing F-02 (N-9)	Part 2	Complete	Yes	05-12-2022	05-12-2022	100	Yes	Yes	Sameday success
ATT & PCC	Praveen Kumar	P2 R.Wall Upto Grade slab (A-1-19)	Part 2	Complete	Yes	05-12-2022	05-12-2022	100	Yes	Yes	Sameday success
ATT & PCC	Praveen Kumar	P2 Footing F-02 (L-9)	Part 2	Complete	Yes	07-12-2022	07-12-2022	100	Yes	Yes	Sameday success
ATT & PCC	Praveen Kumar	P2 Footing F-11 (K-14)	Part 2	Complete	Yes	07-12-2022	07-12-2022	100	Yes	Yes	Sameday success
Total								73018			

Reason For Variances

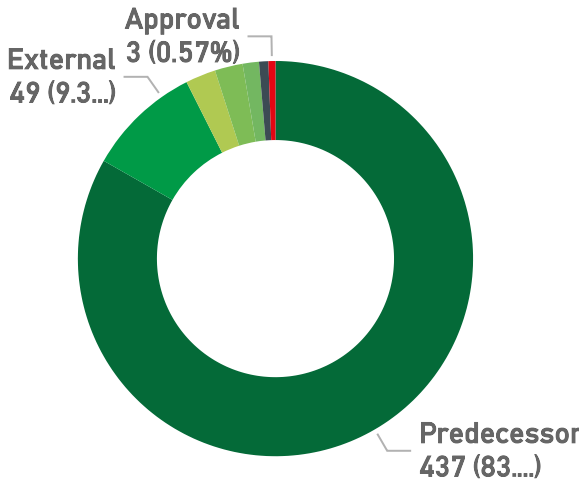

Daily_Weekly PPC
(Planned Date)

Daily_Weekly PPC
(Baseline Date)

Delay analysis (by
Planned)

Delay analysis (by
Baseline)

Activities Not Made
Ready

S Curve (Planned)

S Curve (Baseline)

S Curve - Planned vs
Baseline Variance

Task History

Duration Curve
(Planned)

Duration S curve (
Baseline)

Delay Activity Details


Delay Activity Details

HiTech - Anand Niketan

Ahmedabad, India

Delay/Ahead Analysis - Delay by Days (Feasibility Plan)

Total tasks by delay by days

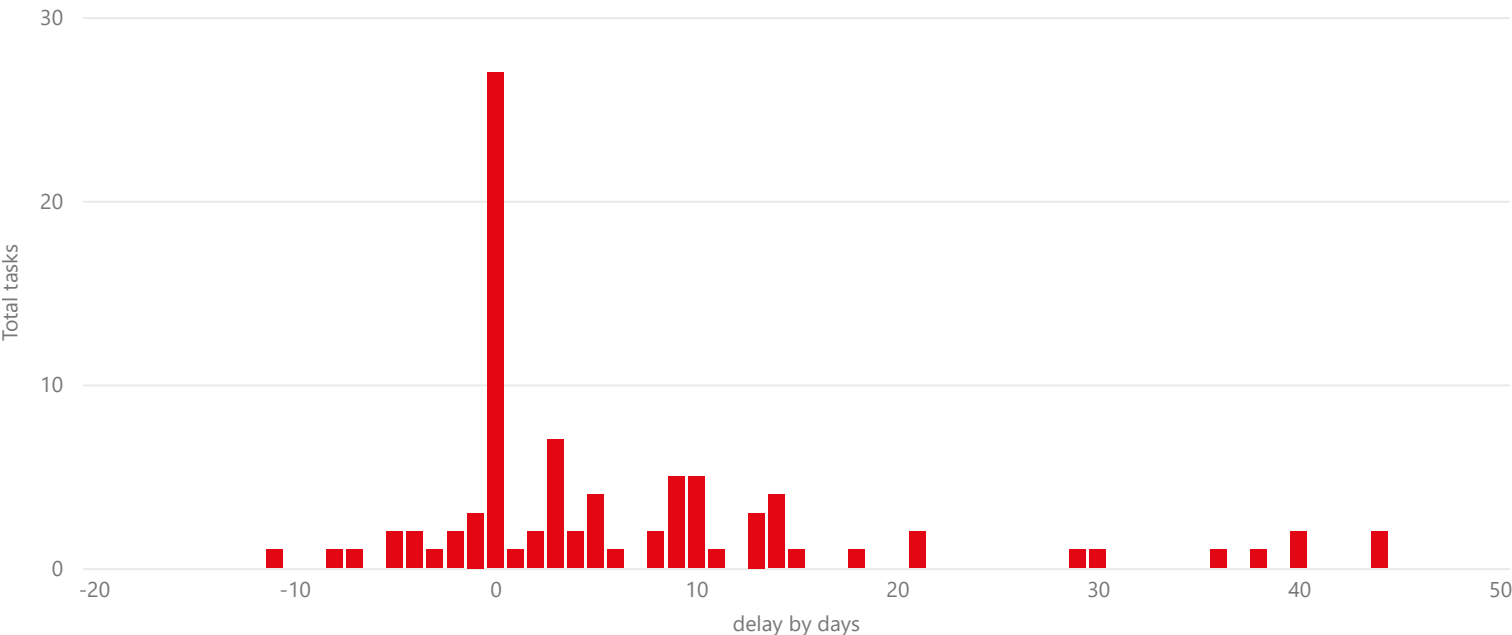

Date

03-02-2023

22-02-2023

Delay By

All

Location

All

Critical Tasks?

All

Owner

All

Distribution of Activities Completed Early/ Late/ On time

Completed Late? Early?	No of Tasks	Distribution %
On Time	27	32.93%
Completed Late	42	51.22%
Completed Early	13	15.85%
Total	82	100.00%

Task Details

ID	Task	Owner	Location	Status	Delay or not	Target	Actual End	customField.Critical Task	delays by days	Target	Actual End	
4983	(P3) Backfilling upto tie beam	Jainam Shah	P3 Foundations/Raft Work	Complete	ontime	07-02-2023	07-02-2023	Yes	0	07-02-2023	07-02-2023	External, Predecessor
4262	(P3) PCC work below Tie Beam	Jainam Shah	P3 Foundations/Raft Work	Complete	Completed Delay	09-02-2023	15-02-2023	Yes	6	09-02-2023	15-02-2023	External, Predecessor
4199	(P4) Backfilling & compaction work upto tie beam	Jignesh Sevara	P4 Backfilling and Compaction of Soil for Floor PCC	Complete	Completed Delay	05-02-2023	21-03-2023	Non Critical	44	05-02-2023	21-03-2023	Manpower not available
4212	(P5) Backfilling & compaction work upto tie beam	Rikesh Kumar Ravi	P5 Backfilling and Compaction of Soil for Floor PCC	Quality checked		16-02-2023	06-03-2023	Non Critical	18	16-02-2023	06-03-2023	Other (Please mention),
5356	(P5) F-5(N-30)	Jainam Shah	P5 Foundations/Raft Work	Complete	Completed Delay	03-02-2023	17-02-2023	Non Critical	14	03-02-2023	17-02-2023	Manpower not available
5352	(P5) F-5(O-29)	Jainam Shah	P5 Foundations/Raft Work	Complete	Completed Delay	03-02-2023	17-02-2023	Non Critical	14	03-02-2023	17-02-2023	Manpower not available
5353	(P5) F-5(O-30)	Jainam Shah	P5 Foundations/Raft Work	Complete	Completed Delay	03-02-2023	18-02-2023	Non Critical	15	03-02-2023	18-02-2023	Manpower not available

HiTech - Anand Niketan

Ahmedabad, India

1172

Total Tasks Due

169

Tasks not ready yet

Activities Due & Not Made Ready

Location

All

Owner

All

Critical Tasks?

All

01-06-2018

30-06-2024

Task Details

Task	Critical?	Owner	Location	Status	Make Ready Date	Planned Start	Planned End	
(P6)R.Wall upto grade slab (out side of Z grid)	Non Critical	Rikesh Kumar Ravi	P6 pedestal	Not Ready	06-02-2023	08-02-2023	11-02-2023	
Part-6 Backfilling & Compaction of Soil for Floor PCC	Non Critical	Rikesh Kumar Ravi	P6 Backfilling and Compaction of Soil for Floor PCC	Not Ready	23-02-2023	25-02-2023	26-02-2023	
Part-6 ATT & PCC work at Basement 2 Floor level	Non Critical	Rikesh Kumar Ravi	P6 ATT and PCC Work	Not Ready	25-02-2023	27-02-2023	01-03-2023	
B2 P4 Beam bottom and shuttering	Non Critical	Arpan Shah	B2 P4 Beam & slab	Not Ready	06-03-2023	08-03-2023	21-03-2023	
B1 P2 Slab Concreitng (A-S-1-18)	Yes	vishal prajapati	B1 P2 Beam & slab	Not Ready	13-03-2023	15-03-2023	15-03-2023	
B2 P4 Slab Reinforcement & Checking	Non Critical	Arpan Shah	B2 P4 Beam & slab	Not Ready	14-03-2023	16-03-2023	27-03-2023	
C53 (S-6) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
C54 (S-8) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
SW1-2 (A-C-03) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
SW14 (G-01) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
SW15 SW16 SW18 (D-H-5-7) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	23-03-2023	
SW17 (D-H-9) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
SW19 (E-13) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
SW3 (B-09) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
SW30 (I-1-11) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	23-03-2023	
SW4 (B-13) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
SW41 (L-3) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	
SW50 SW51 SW52 SW53 SW54 (P-O-2-11) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	23-03-2023	
SW56 (S-2) GF P2	Yes	vishal prajapati	GF P2 verticals	Not Ready	14-03-2023	16-03-2023	20-03-2023	

Total



- Daily_Weekly
PPC (Planned
Date)
- Daily_Weekly
PPC (Baseline
Date)
- Delay analysis
(by Planned)
- Delay analysis
(by Baseline)
- Activities Not
Made Ready
- S Curve
(Planned)
- S Curve
(Baseline)
- S Curve -
Planned vs
Baseline...
- Task History
- Duration Curve
(Planned)
- Duration S curve
(Baseline)
- Delay Activity
Details
- Delay Activity
Details

HiTech - Anand Niketan

Ahmedabad, India

Location (Pours)

▼

All

▼

Critical Tasks?

▼

All

▼

Project Delay/Ahead by

43


Days

19/05/2024


Latest Completion Date

22.48 % Actual completed


28.56 % Progress as per plan...

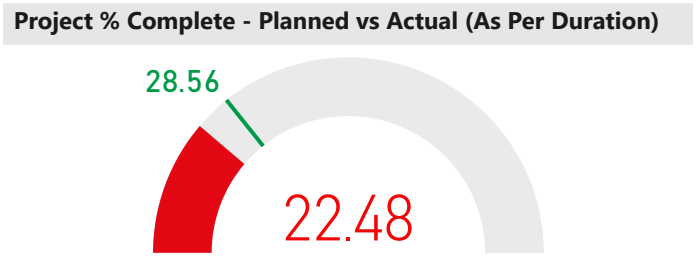


S Curve - End Date Count Baseline vs Actual & Forecast

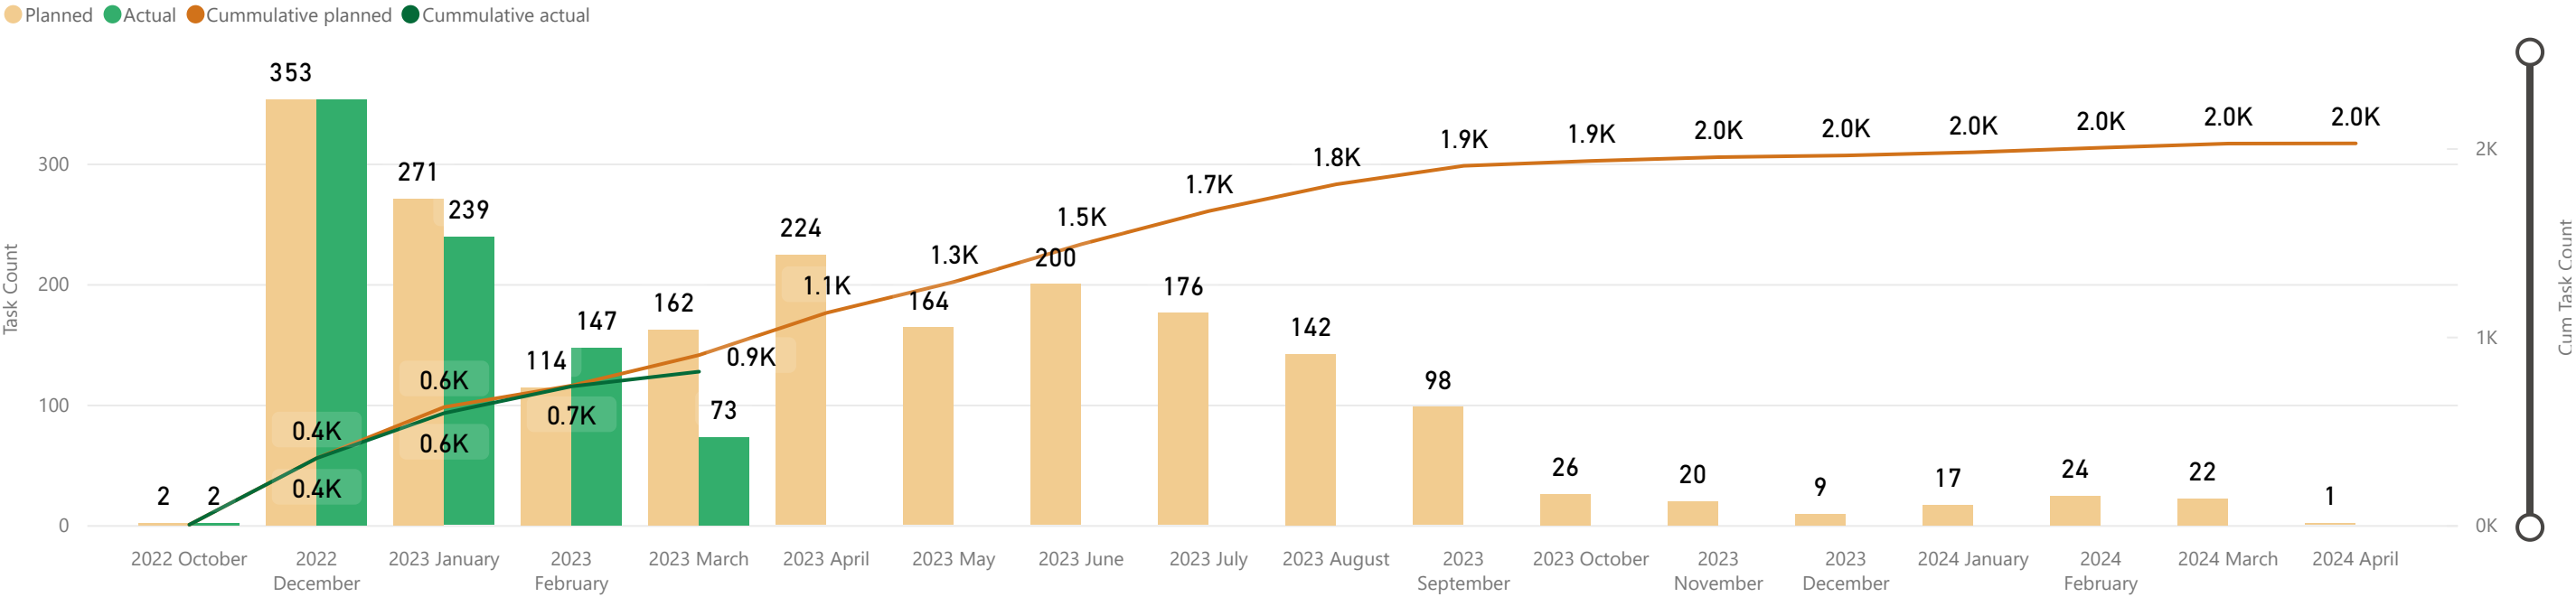

Reason For Variances

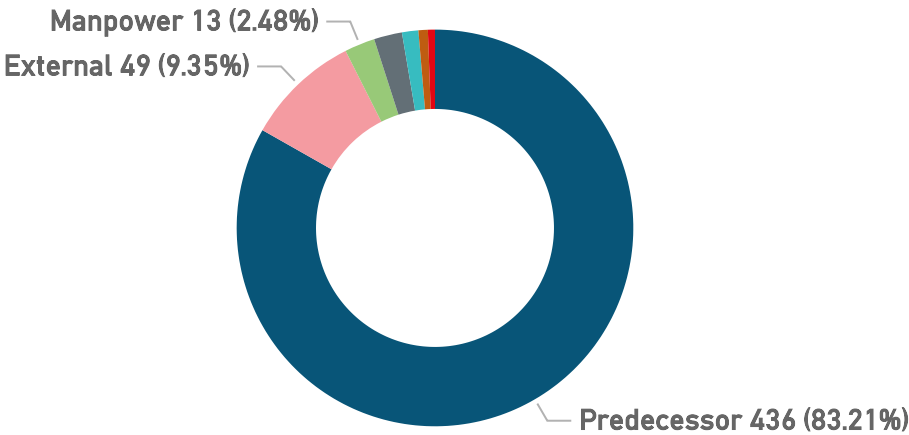

Reasons for Variance by Month

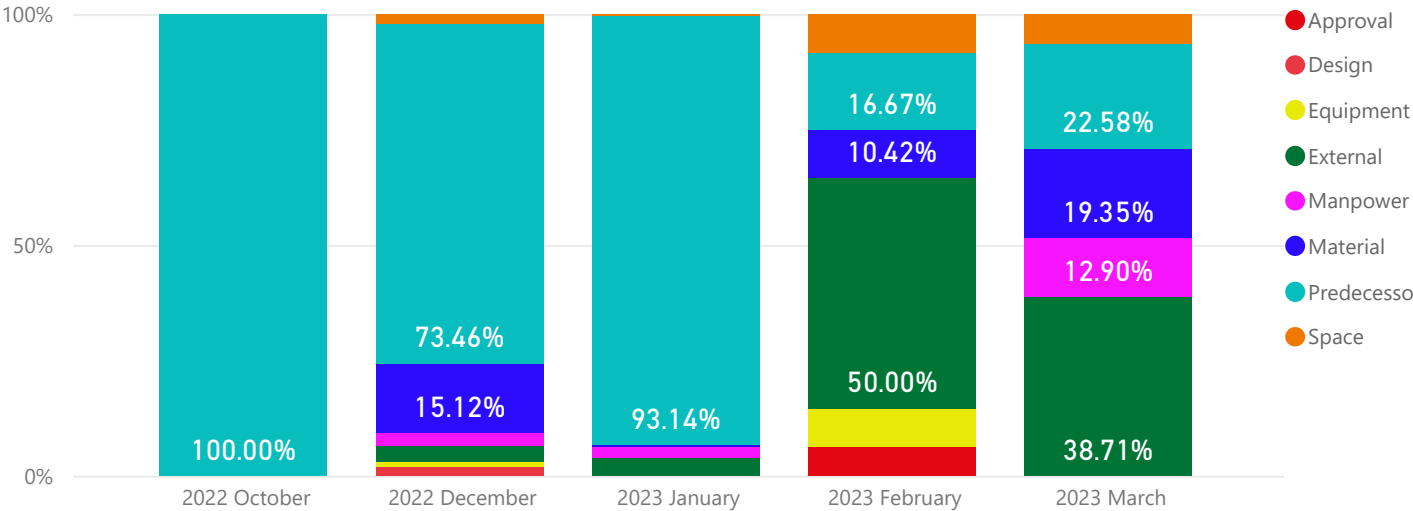

HiTech - Anand Niketan

Ahmedabad, India

Most frequent Actions by Users

Location

All

HistoryType

All

Sub Contractor

All

Building


All

Year


All

Month

All

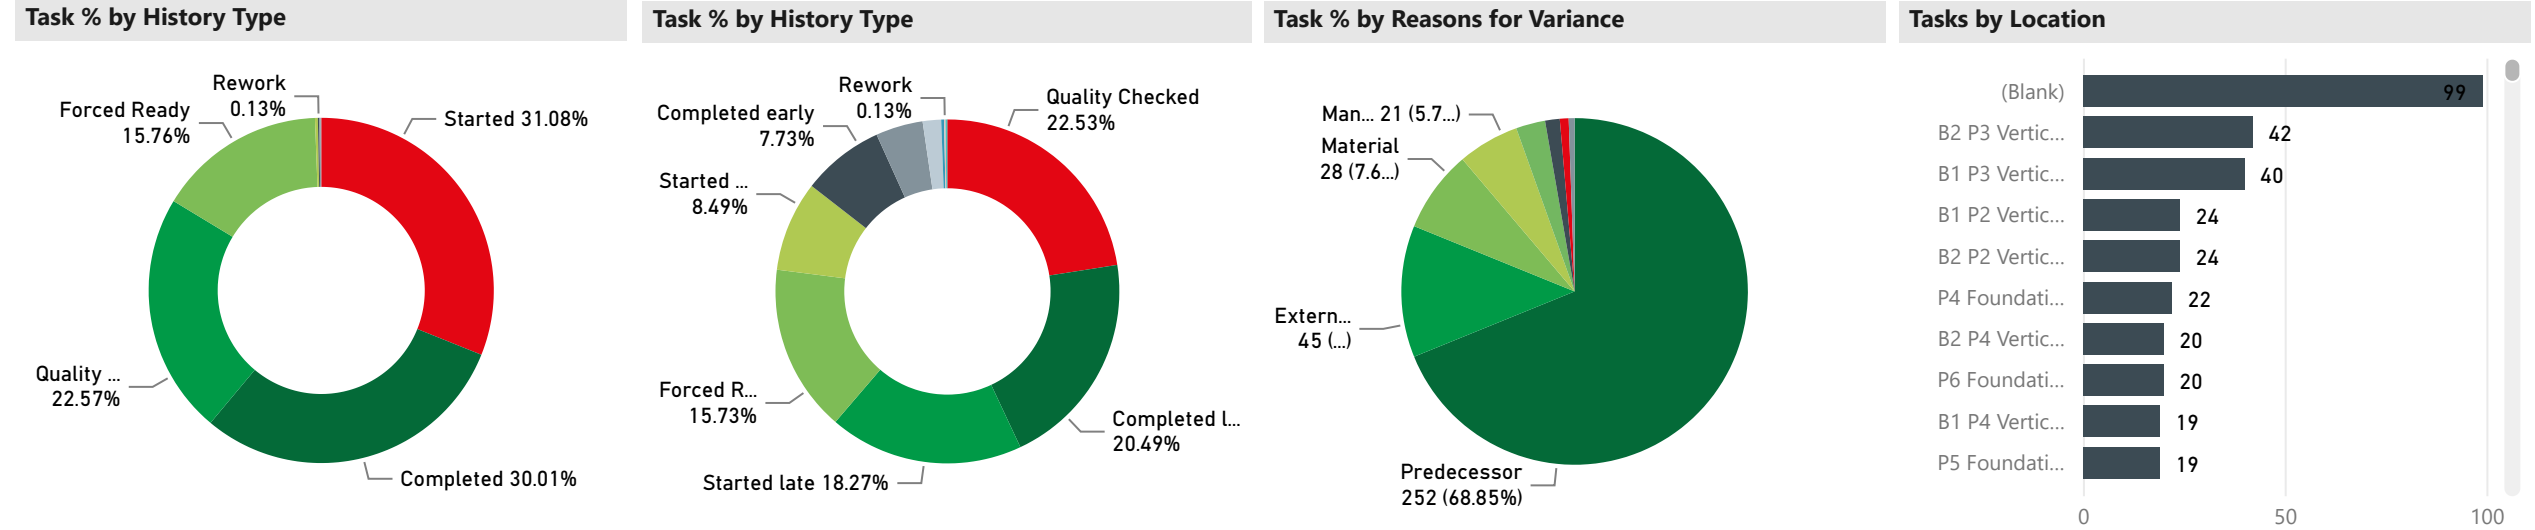

Task Detail										
taskName	status	location	BL StartDate	BL EndDate	PL StartDate	PL EndDate	AC StartDate	AC EndDate	BL End Variance Days	PL
(P1) Dressing & Levelling	Complete	P1 Foundations/Raft Work			14-11-2022	24-12-2022	14-11-2022	24-12-2022	-44919	
(P1) Dressing & Levelling	Complete	P1 Foundations/Raft Work			14-11-2022	24-12-2022	14-11-2022	24-12-2022	-44919	
(P1) Dressing & Levelling	Complete	P1 Foundations/Raft Work			14-11-2022	24-12-2022	14-11-2022	24-12-2022	-44919	
(P1) Dressing & Levelling	Complete	P1 Foundations/Raft Work			14-11-2022	24-12-2022	14-11-2022	24-12-2022	-44919	
(P1) Dressing & Levelling	Complete	P1 Foundations/Raft Work			14-11-2022	24-12-2022	14-11-2022	24-12-2022	-44919	
(P5)C51 (O-30)	Complete	P5 pedestal			04-02-2023	07-02-2023	19-02-2023	21-02-2023	-44978	
(P5)C51 (O-30)	Complete	P5 pedestal			04-02-2023	07-02-2023	19-02-2023	21-02-2023	-44978	
(P5)C51 (O-30)	Complete	P5 pedestal			04-02-2023	07-02-2023	19-02-2023	21-02-2023	-44978	
ATT & PCC	Complete	P3 Footing F4A (W-24)			12-12-2022	12-12-2022	12-12-2022	12-12-2022	-44907	
Total										

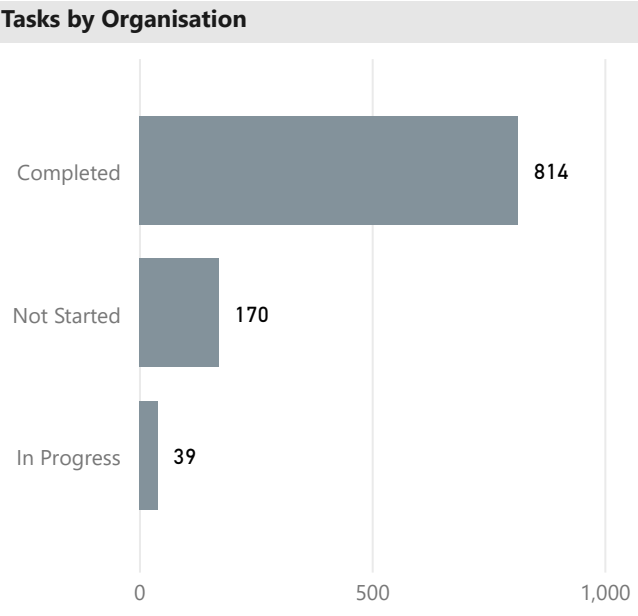

HiTech - Anand Niketan

Ahmedabad, India

Location (Pours)

All

Critical Tasks?

All

Project Delay by

43

Days


19/05/2024

Latest Completion Date

22.48 % Actual completed


28.56 % Progress as per planned

Project % Complete - Planned vs Actual (As Per Duration)




S Curve - End Date Count Baseline vs Actual & Forecast


Sum of Planned Duration * Planned Complete% Sum of Planned Duration * Actual Complete% Cumulative actual completion with planned duration Cumulative planned completion with planned duration

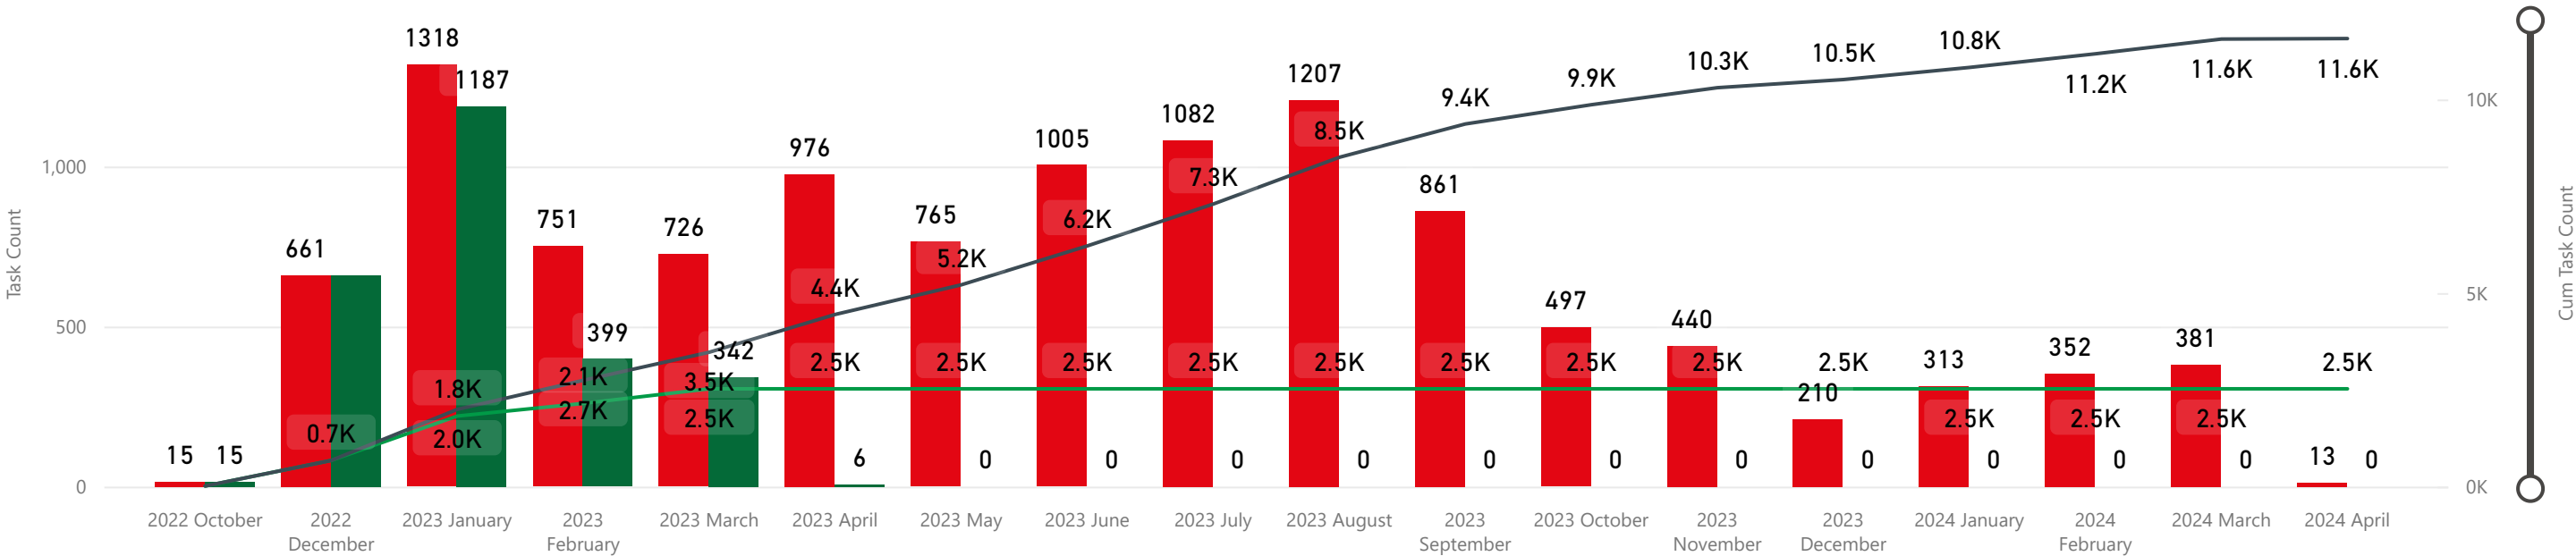

Reason For Variances

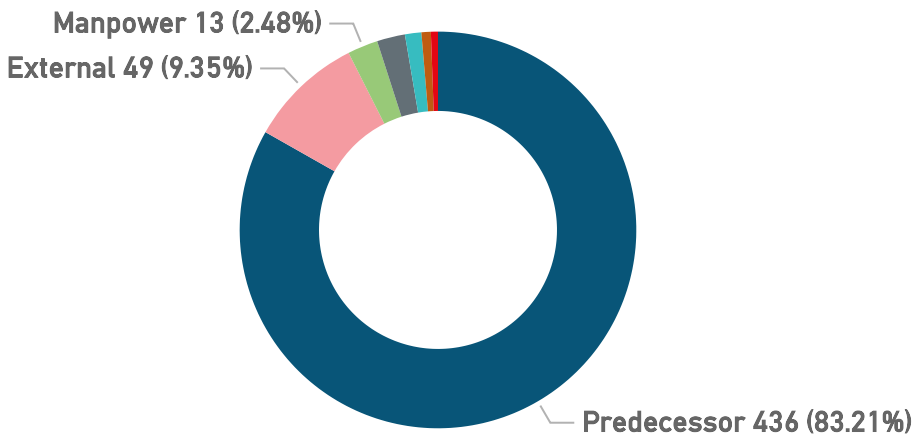

Reasons for Variance by Month

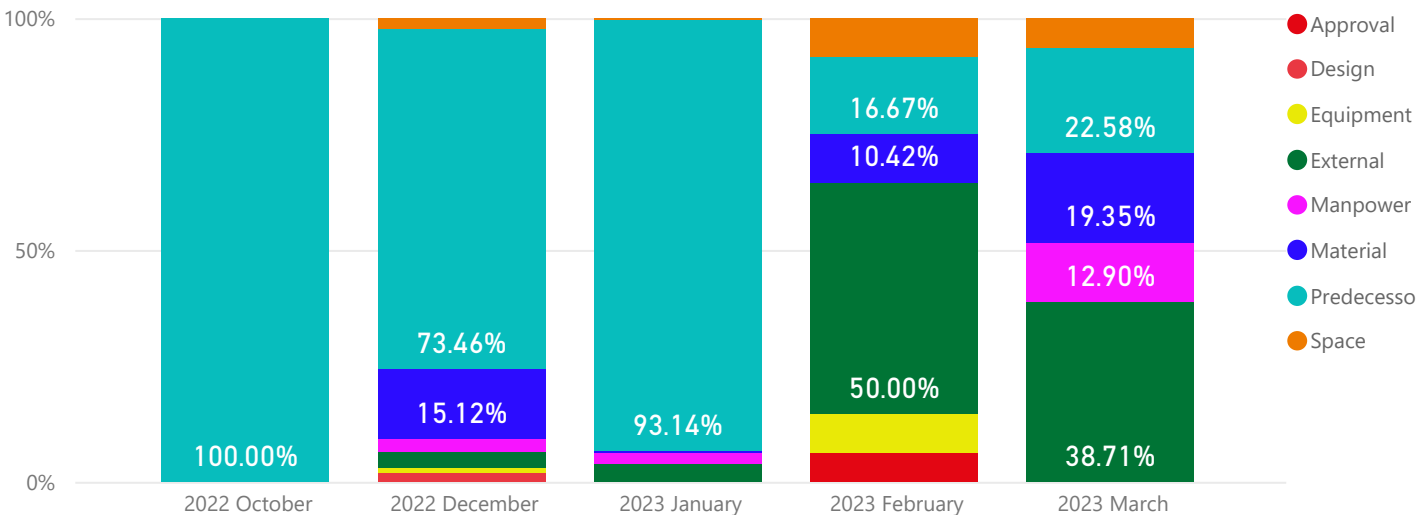

Daily_Weekly PPC
(Planned Date)

Daily_Weekly PPC
(Baseline Date)

Delay analysis (by
Planned)

Delay analysis (by
Baseline)

Activities Not
Made Ready

S Curve (Planned)

S Curve (Baseline)

S Curve - Planned
vs Baseline
Variance

Task History

Duration Curve
(Planned)

Duration S curve (
Baseline)

Delay Activity
Details

Delay Activity
Details



externalId	taskName	owner	Critical Task	Location	status	baselineStartDate	baselineEndDate	actualStartDate	actualEndDate
4387	(P1) Backfilling upto tie beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	11-12-2022	20 December 2022	08-12-2022	26-12-2022
4256	(P1) Concreting for tie beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	26-12-2022	31 December 2022	03-01-2023	10-01-2023
4136	(P1) Dressing & Levelling	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete			14-11-2022	24-12-2022
4255	(P1) Formwork for tie beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	24-12-2022	29 December 2022	29-12-2022	10-01-2023
4252	(P1) PCC work below Tie Beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	21-12-2022	22 December 2022	27-12-2022	27-12-2022
4254	(P1) Reinforcement Work for tie beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	22-12-2022	28 December 2022	27-12-2022	03-01-2023
4604	(P2) Backfilling upto up to tie beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	20-12-2022	29 December 2022	08-12-2022	30-12-2022
4261	(P2) Concreting for tie beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	04-01-2023	09 January 2023	08-01-2023	17-01-2023
4260	(P2) Formwork for tie beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	02-01-2023	07 January 2023	02-01-2023	11-01-2023
4257	(P2) PCC work below Tie Beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	30-12-2022	31 December 2022	26-12-2022	26-12-2022
4259	(P2) Reinforcement Work for tie beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	31-12-2022	06 January 2023	03-01-2023	10-01-2023
4983	(P3) Backfilling upto tie beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	15-12-2022	24 December 2022	08-01-2023	07-02-2023
4266	(P3) Concreting for tie beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	30-12-2022	04 January 2023	21-01-2023	17-02-2023
4163	(P3) Dressing & Levelling	Jayesh Lakhatariya	Yes	P3 Foundations/Raft Work	Complete	23-11-2022	24 November 2022	14-11-2022	02-12-2022
4265	(P3) Formwork for tie beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	28-12-2022	03 January 2023	19-01-2023	16-02-2023
4262	(P3) PCC work below Tie Beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	25-12-2022	26 December 2022	17-01-2023	15-02-2023
4264	(P3) Reinforcement Work for tie beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	26-12-2022	01 January 2023	18-01-2023	15-02-2023
4190	(P4) ATT	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	20-12-2022	20 December 2022	23-12-2022	31-12-2022
4275	(P4) Formwork for tie beam	Jainam Shah	Non Critical	P4 Foundations/Raft Work	Complete	25-01-2023	31 January 2023	09-02-2023	25-02-2023
4274	(P4) Reinforcement Work for tie beam	Jainam Shah	Non Critical	P4 Foundations/Raft Work	Complete	23-01-2023	30 January 2023	09-02-2023	24-02-2023
4199	(P4) Backfilling & compaction work upto tie beam	Jignesh Sevara	Non Critical	P4 Backfilling and Compaction of Soil for Floor PCC	Complete	22-01-2023	23 January 2023	26-01-2023	21-03-2023
5348	(P4) C16 (L-24.1)	Rikesh Kumar Ravi	Non Critical	P4 Pedestal	Complete	01-01-2023	04 January 2023	19-01-2023	21-01-2023
4276	(P4) Concreting for tie beam	Jainam Shah	Non Critical	P4 Foundations/Raft Work	Complete	28-01-2023	02 February 2023	10-02-2023	28-02-2023
4189	(P4) Dressing & Levelling	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	20-12-2022	21 December 2022	21-12-2022	21-12-2022
5324	(P4) F-12(N-22)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	01-01-2023	05 January 2023	16-01-2023	18-01-2023
5323	(P4) F-12(N-24.1)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	01-01-2023	05 January 2023	30-12-2022	20-01-2023
5325	(P4) F-13(N-19)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	01-01-2023	05 January 2023	30-12-2022	20-01-2023
5334	(P4) F-14(L-19)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	24-12-2022	28 December 2022	04-01-2023	18-01-2023
5329	(P4) F-14(M-19)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	28-12-2022	01 January 2023	04-01-2023	18-01-2023



externalId	taskName	owner	Critical Task	Location	status	plannedStartDate	plannedEndDate	actualStartDate	actualEndDate
4387	(P1) Backfilling upto tie beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	08-12-2022	26-12-2022	08-12-2022	26-12-2022
4256	(P1) Concreting for tie beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	03-01-2023	10-01-2023	03-01-2023	10-01-2023
4136	(P1) Dressing & Levelling	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	14-11-2022	24-12-2022	14-11-2022	24-12-2022
4255	(P1) Formwork for tie beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	29-12-2022	10-01-2023	29-12-2022	10-01-2023
4252	(P1) PCC work below Tie Beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	27-12-2022	27-12-2022	27-12-2022	27-12-2022
4254	(P1) Reinforcement Work for tie beam	Praveen Kumar	Yes	P1 Foundations/Raft Work	Complete	27-12-2022	03-01-2023	27-12-2022	03-01-2023
4604	(P2) Backfilling upto up to tie beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	08-12-2022	30-12-2022	08-12-2022	30-12-2022
4261	(P2) Concreting for tie beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	08-01-2023	17-01-2023	08-01-2023	17-01-2023
4260	(P2) Formwork for tie beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	02-01-2023	11-01-2023	02-01-2023	11-01-2023
4257	(P2) PCC work below Tie Beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	26-12-2022	26-12-2022	26-12-2022	26-12-2022
4259	(P2) Reinforcement Work for tie beam	Praveen Kumar	Yes	P2 Foundations/Raft Work	Complete	03-01-2023	10-01-2023	03-01-2023	10-01-2023
4983	(P3) Backfilling upto tie beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	08-01-2023	07-02-2023	08-01-2023	07-02-2023
4266	(P3) Concreting for tie beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	21-01-2023	28-01-2023	21-01-2023	17-02-2023
4163	(P3) Dressing & Levelling	Jayesh Lakhatariya	Yes	P3 Foundations/Raft Work	Complete	14-11-2022	02-12-2022	14-11-2022	02-12-2022
4265	(P3) Formwork for tie beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	19-01-2023	27-01-2023	19-01-2023	16-02-2023
4262	(P3) PCC work below Tie Beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	17-01-2023	09-02-2023	17-01-2023	15-02-2023
4264	(P3) Reinforcement Work for tie beam	Jainam Shah	Yes	P3 Foundations/Raft Work	Complete	18-01-2023	25-01-2023	18-01-2023	15-02-2023
4190	(P4) ATT	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	23-12-2022	31-12-2022	23-12-2022	31-12-2022
4275	(P4) Formwork for tie beam	Jainam Shah	Non Critical	P4 Foundations/Raft Work	Complete	07-01-2023	12-01-2023	09-02-2023	25-02-2023
4274	(P4) Reinforcement Work for tie beam	Jainam Shah	Non Critical	P4 Foundations/Raft Work	Complete	05-01-2023	11-01-2023	09-02-2023	24-02-2023
4199	(P4) Backfilling & compaction work upto tie beam	Jignesh Sevara	Non Critical	P4 Backfilling and Compaction of Soil for Floor PCC	Complete	26-01-2023	05-02-2023	26-01-2023	21-03-2023
5348	(P4) C16 (L-24.1)	Rikesh Kumar Ravi	Non Critical	P4 Pedestal	Complete	19-01-2023	21-01-2023	19-01-2023	21-01-2023
4276	(P4) Concreting for tie beam	Jainam Shah	Non Critical	P4 Foundations/Raft Work	Complete	09-01-2023	15-01-2023	10-02-2023	28-02-2023
4189	(P4) Dressing & Levelling	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	21-12-2022	21-12-2022	21-12-2022	21-12-2022
5324	(P4) F-12(N-22)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	16-01-2023	18-01-2023	16-01-2023	18-01-2023
5323	(P4) F-12(N-24.1)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	30-12-2022	20-01-2023	30-12-2022	20-01-2023
5325	(P4) F-13(N-19)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	30-12-2022	20-01-2023	30-12-2022	20-01-2023
5334	(P4) F-14(L-19)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	04-01-2023	18-01-2023	04-01-2023	18-01-2023
5329	(P4) F-14(M-19)	Rikesh Kumar Ravi	Non Critical	P4 Foundations/Raft Work	Complete	04-01-2023	18-01-2023	04-01-2023	18-01-2023
